

Jones AT&T Stadium North End Zone Facilities



Exterior View of the Concession Stands

Scope: This project constructed 7,000 GSF Build-Out under the seating stands including toilets and concessions. Project provided an additional 24 WCs for women and 21 plumbing fixtures for men; 6 lavatories for women and 5 for men. Project also included concessions infrastructure and build out by Ovations.

Budget: \$1,300,000.00

Actual Cost: \$1,044,850.07

Schedule: Starts: May 17, 2010
Substantial Completion: Sept 17, 2011

Architect: Ross John Narvaeth, AIA


Contractor: Lee Lewis Construction



View of the Stadium



View within the Concession

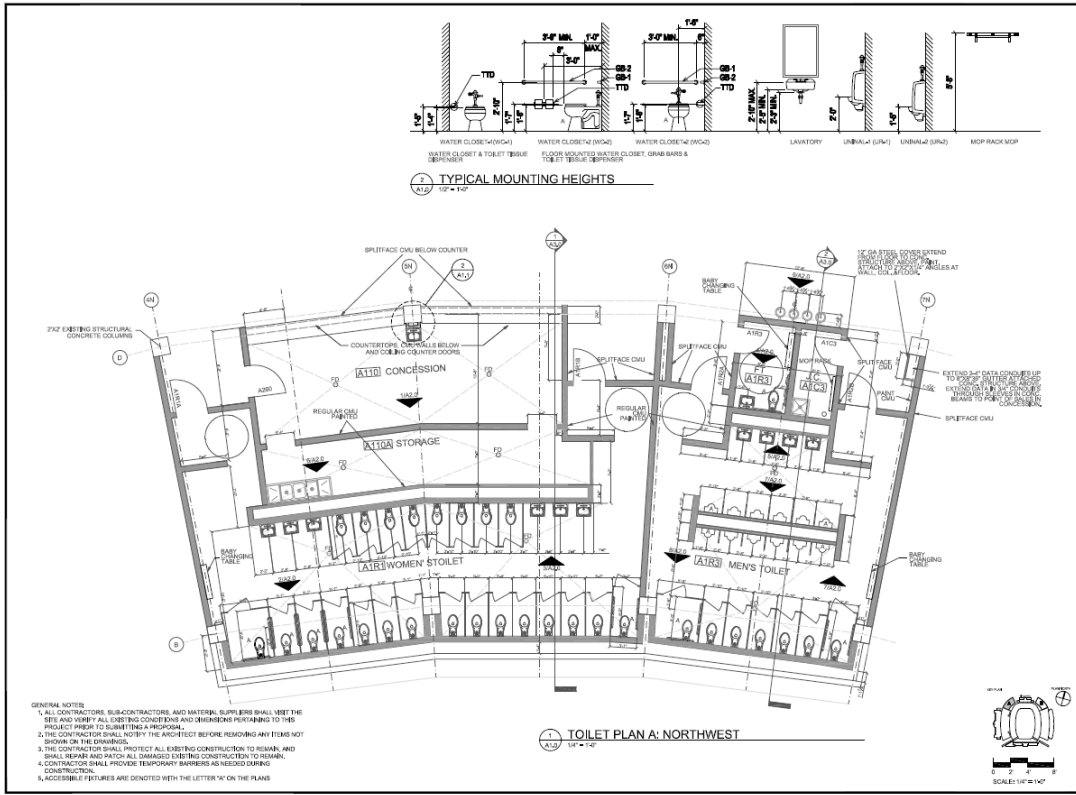

FACILITIES

ROSS JOHN NARVAETH, AIA

Project Architect

1000 University Blvd, Suite 100

Fort Worth, Texas 76102

Phone: 817.798.1111

Fax: 817.798.1112

www.rossjohnnarvaeth.com

JONES AT&T STADIUM

NORTH END ZONE FACILITIES

1000 University Blvd, Suite 100

Fort Worth, Texas 76102

Phone: 817.798.1111

Fax: 817.798.1112

www.rossjohnnarvaeth.com

NO.	DESCRIPTION	DATE
1	ISSUED FOR BIDDING	07/20/10
2	REVISION	
3	REVISION	
4	REVISION	
5	REVISION	
6	REVISION	
7	REVISION	
8	REVISION	
9	REVISION	
10	REVISION	

PROJECT NO: 0705070

DATE: 07/20/10

DESIGNER: [Signature]

CHECKED BY: [Signature]

DATE: 07/20/10

SCALE: 1/8" = 1'-0"

AREA A

A1.0

Concessions and Toilet Room Floor Plan



View of the Toilet Stalls



View of the Lavatories
